



PROGRAMS


| CPGRAMS | | State | | District | | Block | |
|----------------------|-------------|---------------------|-------------|---------------------|-------------|---------------------|-------------|
| All | | All | | All | | All | |
| MoRD Target (in No.) | 2,67,38,031 | Registered (in No.) | 2,62,38,093 | Geo-Tagged (in No.) | 2,43,25,226 | Sanctioned (in No.) | 1,86,46,130 |
| Completed (in No.) | | | | | | | |

Data Last refreshed on: 01-Jul-2022
[Report](#)

| Overview | Allottee type | Completion Span Analysis | Geological/Geo-spatial analysis | Transaction Type Delays | Physically Completed houses pending for Financial Completion | Landless | Stagewise Delay |
|-------------------------------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|
| Target Report | | | | | | | |


Select House Status: [MoRD Target](#) [Registered](#) [Geo-Tagged](#) [Sanctioned](#) [Completed](#)

House Construction Status - Cumulative

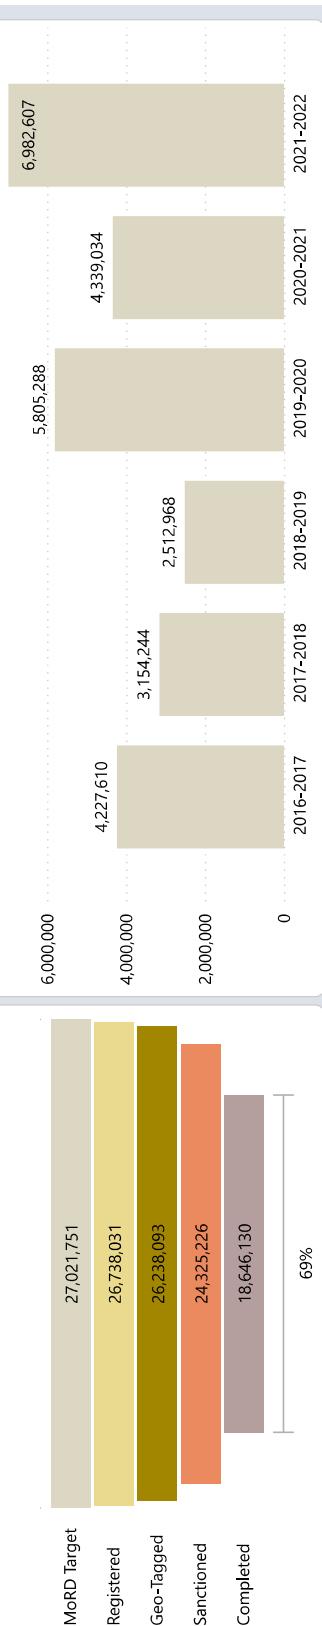

Social Category

Construction Status by Social Category - Cumulative

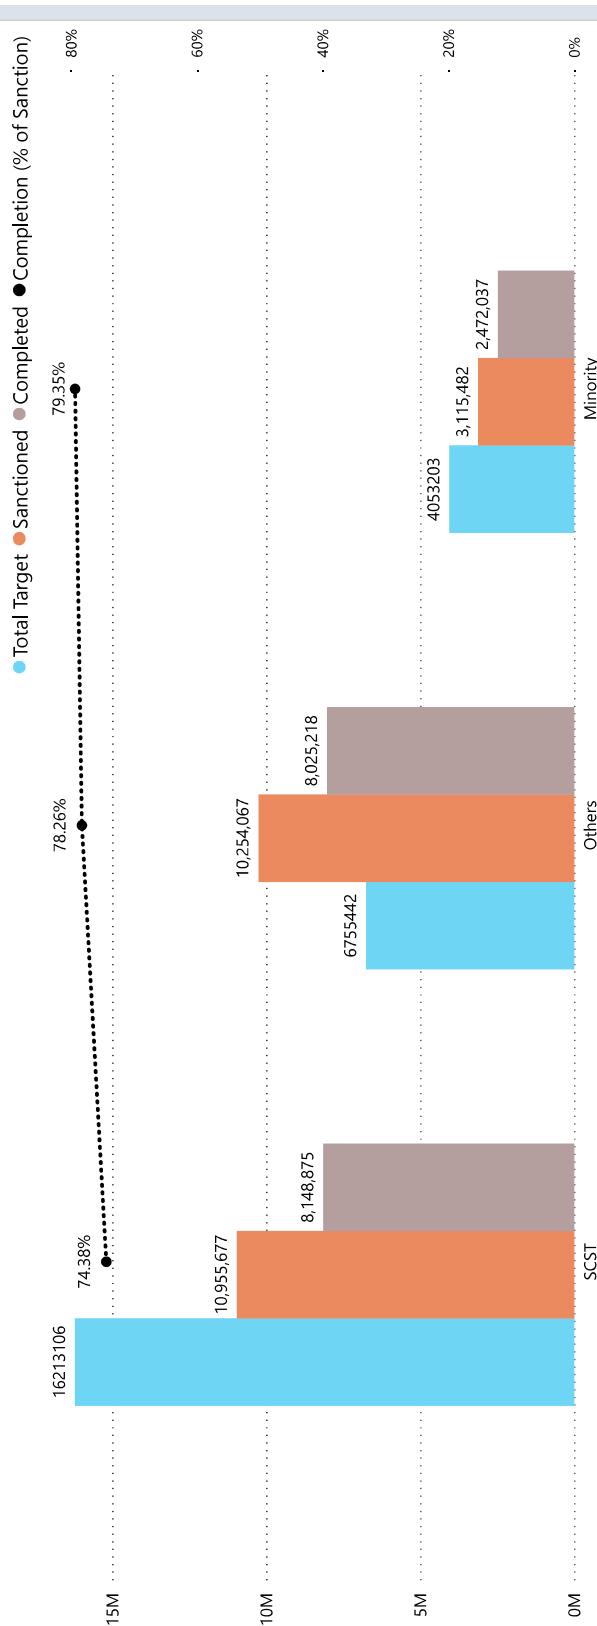



CPGRAMS

State

All

District

All

Block


All

| MoRD Target (in No.) | Registered (in No.) | Geo-Tagged (in No.) | Sanctioned (in No.) | Completed (in No.) | Data Last refreshed on: 01-Jul-2022 |
|----------------------|---------------------|---------------------|---------------------|--------------------|-------------------------------------|
| 2,70,21,751 | 2,67,35,989 | 2,62,36,069 | 2,43,23,228 | 1,86,44,184 | |


| Overview | Allottee type | Completion Span Analysis | Geological/Geo-spatial analysis | Transaction Type Delays | Physically Completed houses pending for Financial Completion | Landless | Stagewise Delay |
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|

Allottee Typewise % Completion - Cumulative


Joint(Husband and Wife) ● Male ● Female ● Transgender

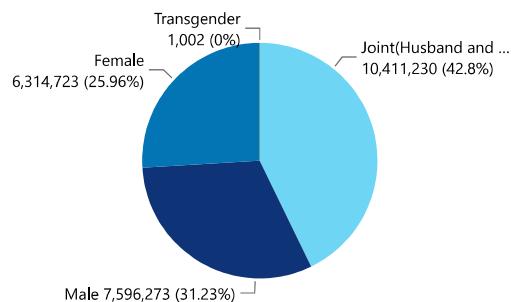**Allottee Typewise Yearwise % Completion**


Joint(Husband and Wife) ● Male ● Female ● Transgender

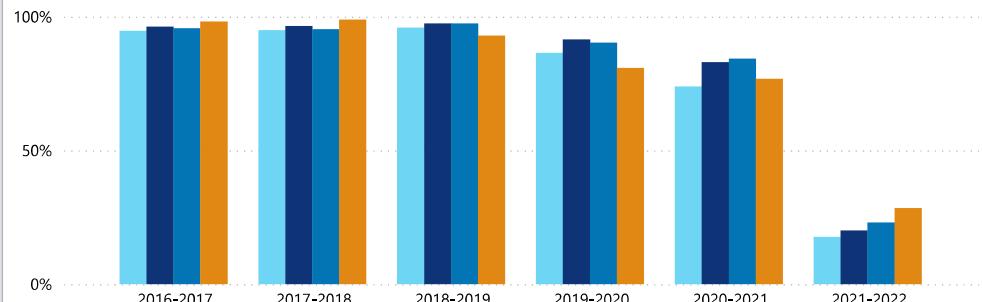**Yearwise % Completion**

● Sanctioned ● Completed ● Completion (% of Sanction)

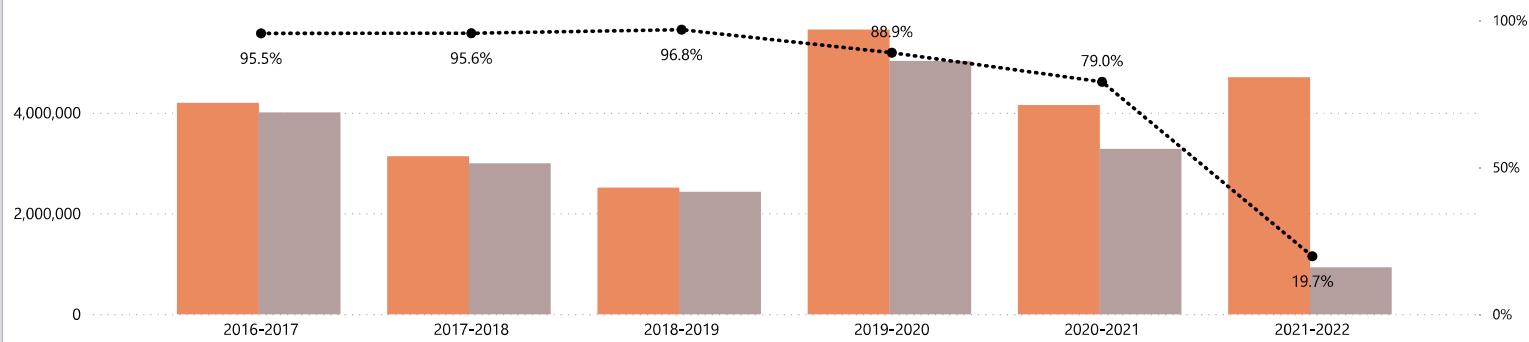**House Completion (% of Sanction) by State and Allottee Type**

Joint(Husband and Wife) ● Male ● Female ● Transgender

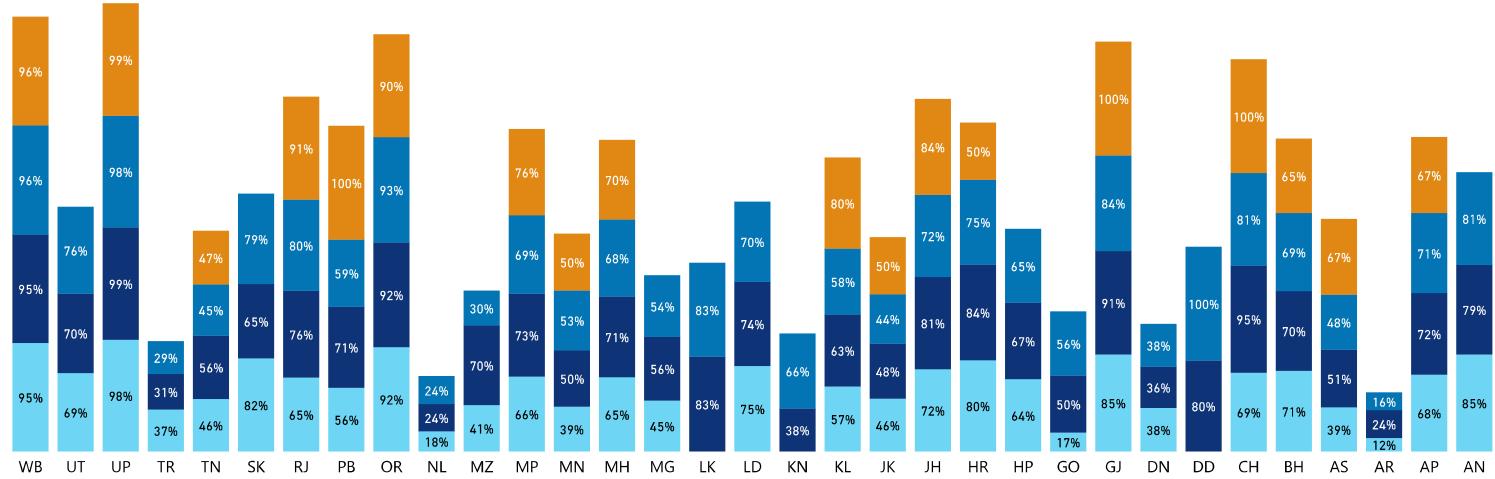



CPGRAMS

State

All

District

All

Block

All

MoRD Target (in No.)

Registered (in No.)

Geo-Tagged (in No.)

Sanctioned (in No.)

Completed (in No.)

Data Last refreshed on: 01-Jul-2022

2,70,21,751

2,67,38,031

2,62,38,093

2,43,25,226

1,86,46,130

[Report](#)

Overview

Allottee type

Completion Span Analysis

Geological/Geo-spatial analysis

Transaction Type Delays


Physically Completed houses pending for Financial Completion

Landless

Stagewise Delay

Houses Completion within 365 day vs after 365 days

● Within 10 months ● Within 10 to 12 months ● In 1-2 years ● In 2-3 years ● After 3 years



Average Completion Time of houses sanctioned under PMAYG

| State | Sanctioned | Completed | Avg Time (in Days) | Completed within 10 months | Within 10 to 12 months | Completed in 1-2 years | Completed in 2-3 years | Completed after 3 years |
|------------------------|-------------------|-------------------|--------------------|----------------------------|------------------------|------------------------|------------------------|-------------------------|
| ANDAMAN AND NICOBAR | 1,355 | 754 | 287 | 486 | 54 | 211 | 3 | 0 |
| ANDHRA PRADESH | 67,567 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| ARUNACHAL PRADESH | 35,089 | 1,868 | 165 | 1,625 | 165 | 73 | 5 | 0 |
| ASSAM | 1,282,496 | 574,328 | 359 | 239,214 | 100,478 | 209,666 | 20,098 | 4872 |
| BIHAR | 3,644,029 | 2,548,223 | 383 | 1,210,951 | 226,482 | 842,124 | 199,810 | 68856 |
| CHHATTISGARH | 1,096,478 | 825,065 | 278 | 578,395 | 79,304 | 150,453 | 14,865 | 2048 |
| DADRA AND NAGAR HAVELI | 5,624 | 2,132 | 468 | 537 | 252 | 922 | 381 | 40 |
| DAMAN AND DIU | 47 | 13 | 84 | 13 | 0 | 0 | 0 | 0 |
| GOA | 242 | 133 | 474 | 34 | 15 | 74 | 10 | 0 |
| GUJARAT | 433,570 | 380,198 | 303 | 248,090 | 36,097 | 75,700 | 18,746 | 1565 |
| HARYANA | 26,793 | 20,914 | 451 | 8,722 | 1,963 | 6,153 | 3,728 | 348 |
| HIMACHAL PRADESH | 15,084 | 9,865 | 304 | 5,205 | 1,567 | 2,885 | 165 | 43 |
| JAMMU AND KASHMIR | 195,260 | 90,557 | 414 | 31,960 | 10,699 | 40,086 | 6,698 | 1114 |
| JHARKHAND | 1,584,039 | 1,205,945 | 310 | 754,391 | 139,571 | 258,636 | 41,284 | 12063 |
| KARNATAKA | 92,687 | 0 | 0 | 0 | 0 | 0 | 0 | 0 |
| KERALA | 34,433 | 20,173 | 320 | 11,058 | 2,600 | 5,891 | 536 | 88 |
| LADAKH | 1,231 | 942 | 210 | 749 | 106 | 87 | 0 | 0 |
| LAKSHADWEEP | 53 | 44 | 771 | 0 | 0 | 23 | 15 | 6 |
| MADHYA PRADESH | 3,677,058 | 2,562,319 | 239 | 2,040,390 | 207,883 | 260,020 | 38,508 | 15518 |
| MAHARASHTRA | 1,243,023 | 825,180 | 322 | 452,677 | 104,388 | 227,238 | 31,635 | 9242 |
| MANIPUR | 34,082 | 15,017 | 457 | 3,449 | 1,708 | 8,494 | 1,010 | 356 |
| MEGHALAYA | 61,633 | 29,609 | 490 | 6,476 | 2,710 | 17,147 | 2,218 | 1058 |
| MIZORAM | 13,532 | 5,511 | 345 | 2,894 | 639 | 1,711 | 235 | 32 |
| NAGALAND | 22,299 | 4,239 | 418 | 923 | 863 | 2,323 | 130 | 0 |
| Total | 24,254,109 | 18,489,662 | 282 | 12,706,670 | 1,743,127 | 3,329,991 | 532,456 | 177418 |



CPGRAMS

State

All

District

All

Block

All

| MoRD Target (in No.) | Registered (in No.) | Geo-Tagged (in No.) | Sanctioned (in No.) | Completed (in No.) |
|----------------------|---------------------|---------------------|---------------------|--------------------|
| 2,70,21,751 | 2,67,38,031 | 2,62,38,093 | 2,43,25,226 | 1,86,46,130 |


Data Last refreshed on: 01-Jul-2022

[Report](#)

| Overview | Allottee type | Completion Span Analysis | Geological/Geo-spatial analysis | Transaction Type Delays | Physically Completed houses pending for Financial Completion | Landless | Stagewise Delay |
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|


House(s) Completed by Region

● Hilly/Difficult ● Plain

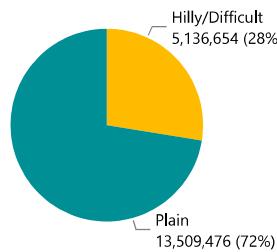

House Completion Status by State and Region

● Sanctioned ● Completed



House Completion (% of Sanction) by State and Region

● Hilly/Difficult ● Plain



Average Completion Time of houses sanctioned under PMAYG


| Season | State | Summer | | | | Rainy | | | | Winter | | | | Spring | | | | |
|------------------------|-------|--------|-----|-----|---------------------|-------|-----|-----|---------------------|--------|-----|-----|---------------------|--------|-----|-----|---------------------|-----|
| | | Apr | May | Jun | Avg Completion Days | Jul | Aug | Sep | Avg Completion Days | Oct | Nov | Dec | Avg Completion Days | Jan | Feb | Mar | Avg Completion Days | |
| ANDAMAN AND NICOBAR | | 339 | 322 | 310 | 310 | 323 | 13 | 311 | 318 | 234 | 203 | 231 | 245 | 228 | 343 | 253 | | |
| ARUNACHAL PRADESH | | 91 | 108 | 243 | 154 | 264 | 161 | 166 | 176 | 103 | 215 | 116 | 112 | 114 | 64 | 193 | 164 | |
| ASSAM | | 400 | 395 | 437 | 409 | 363 | 344 | 320 | 340 | 325 | 342 | 321 | 330 | 297 | 353 | 403 | 354 | |
| BIHAR | | 295 | 353 | 388 | 364 | 425 | 420 | 401 | 416 | 397 | 425 | 355 | 392 | 340 | 373 | 292 | 334 | |
| CHHATTISGARH | | 235 | 242 | 273 | 263 | 239 | 228 | 427 | 303 | 284 | 231 | 220 | 251 | 253 | 280 | 252 | 270 | |
| DADRA AND NAGAR HAVELI | | 476 | 394 | 492 | 471 | 363 | 159 | | 352 | 388 | 470 | 526 | 492 | 474 | 436 | 477 | 467 | |
| DAMAN AND DIU | | | | | | | | | | | | | | | | 84 | 84 | |
| GOA | | | | | 649 | 649 | 381 | 405 | 385 | 391 | 511 | 482 | 418 | 493 | 445 | 159 | 663 | 484 |
| GUJARAT | | 291 | 324 | 343 | 329 | 369 | 292 | 319 | 326 | 251 | 237 | 218 | 243 | 295 | 155 | 312 | 279 | |
| HARYANA | | 461 | 541 | 448 | 483 | 385 | 422 | 337 | 386 | 534 | 519 | 413 | 497 | 438 | 579 | 371 | 424 | |
| HIMACHAL PRADESH | | 247 | 301 | 262 | 268 | 344 | 413 | 304 | 389 | 460 | 255 | 392 | 419 | 217 | 241 | 275 | 265 | |
| JAMMU AND KASHMIR | | 423 | 403 | 422 | 420 | 405 | 378 | 432 | 414 | 436 | 404 | 387 | 418 | 421 | 329 | 410 | 402 | |
| JHARKHAND | | 365 | 325 | 320 | 332 | 332 | 316 | 279 | 312 | 250 | 277 | 275 | 263 | 301 | 348 | 366 | 338 | |
| KERALA | | 354 | 338 | 342 | 345 | 269 | 279 | 249 | 265 | 263 | 267 | 266 | 266 | 284 | 323 | 364 | 335 | |
| Total | | 227 | 224 | 192 | 212 | 95 | 75 | 190 | 122 | 245 | 255 | 212 | 269 | 166 | 272 | 214 | 273 | |

| MoRD Target (in No.) | Registered (in No.) | Geo-Tagged (in No.) | Sanctioned (in No.) | Completed (in No.) | Data Last refreshed on: 01-Jul-2022 |
|----------------------|---------------------|---------------------|---------------------|--------------------|-------------------------------------|
| 2,70,21,751 | 2,67,38,031 | 2,62,38,093 | 2,43,25,226 | 1,86,46,130 | Report |

| Overview | Allottee type | Completion Span Analysis | Geological/Geo-spatial analysis | Transaction Type Delays | Physically Completed houses pending for Financial Completion | Landless | Stagewise Delay |
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|
|----------|---------------|--------------------------|---------------------------------|-------------------------|--|----------|-----------------|


Total time taken by Year and Phase (Days)

● Administrative Time ● Financial Transaction Time ● Construction Time

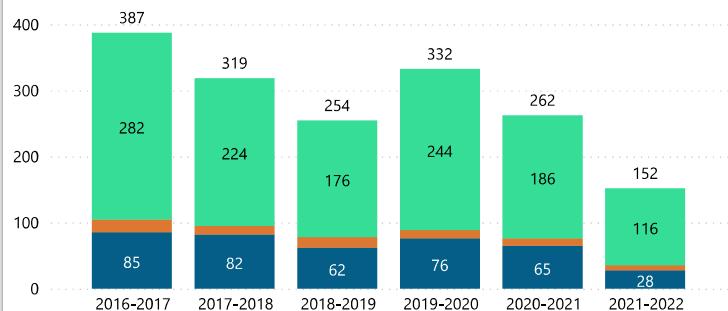


House Construction Time Phase

Administrative Time | Financial Transaction Time | Construction Time

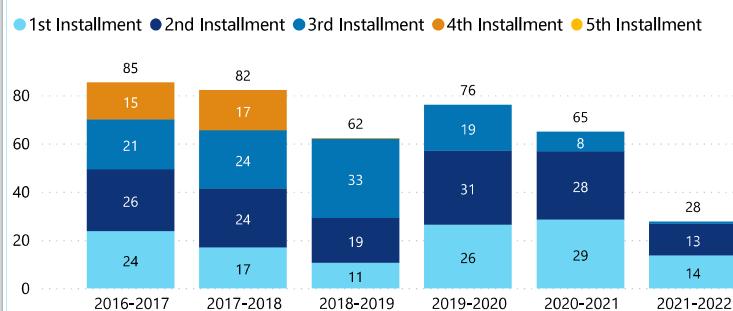


Social Category

Average Administrative Time taken by Social Category - Cumulative (Days)

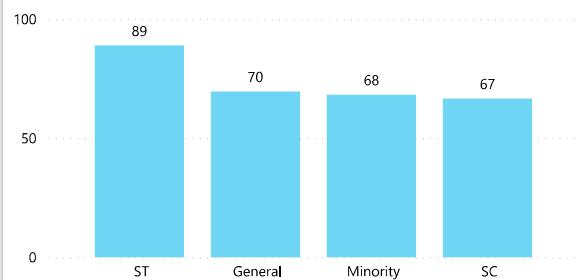


Average time taken by Social Category - Cummulative (Days)

● Administrative Time ● Financial Transaction Time ● Construction Time

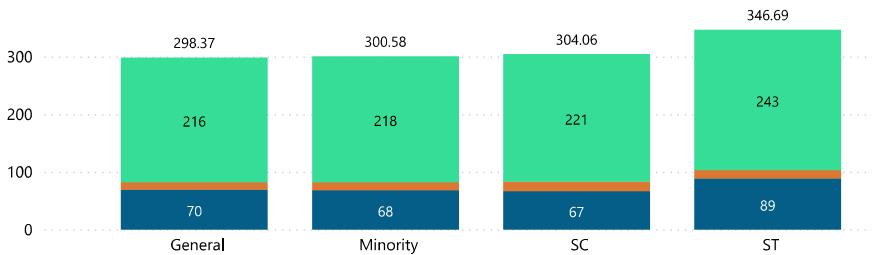


Average time taken (in cumulative days) - State/District/Blockwise comparison - Cummulative

● Administrative Time ● Financial Transaction Time ● Construction Time

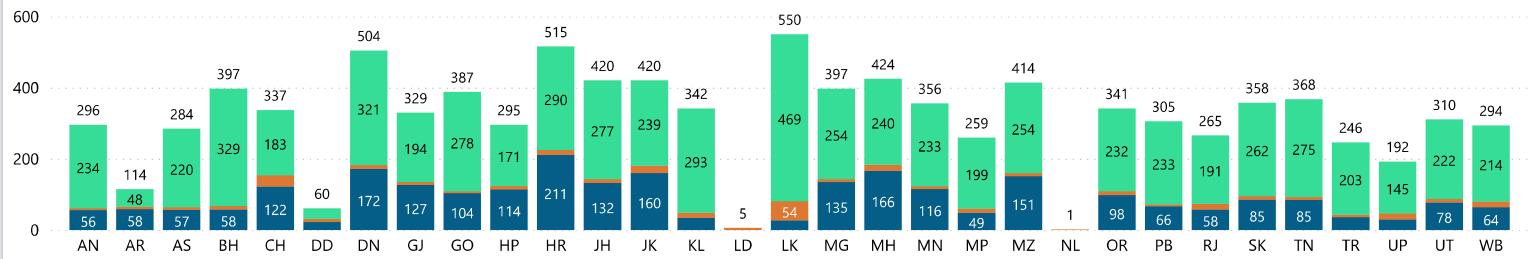

States with Average Completion time greater than 365 days

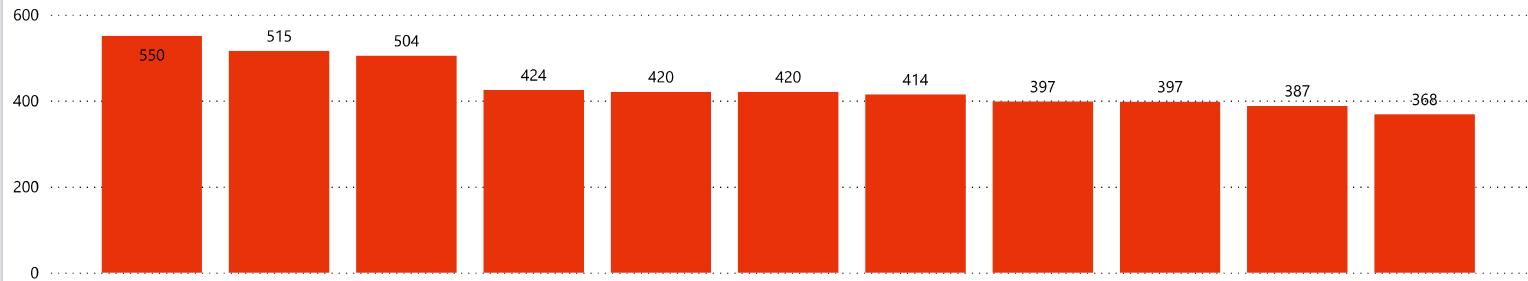



CPGRAMS

State

All

District

All

Block

All

MoRD Target (in No.)

Registered (in No.)

Geo-Tagged (in No.)

Sanctioned (in No.)

Completed (in No.)

Data Last refreshed on: 01-Jul-2022

2,70,21,751

2,67,38,031

2,62,38,093

2,43,25,226

1,86,46,130

[Report](#)

Overview

Allottee type

Completion Span Analysis

Geological/Geo-spatial analysis

Transaction Type Delays


Physically Completed houses pending for Financial Completion

Landless

Stagewise Delay


Completed houses vs Installment Release

● House Completed and Amount Released Fully ● House Completed but Amount Released partially




Completed houses vs Installment Release


● House Completed and Amount Released Fully ● House Completed but Amount Released partially




House Completed but installment amount remaining to be paid (Rs in Lakhs)

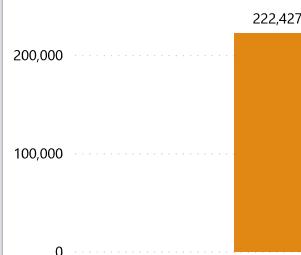


House Completed but installment amount remaining to be paid by year (Rs in Lakhs)

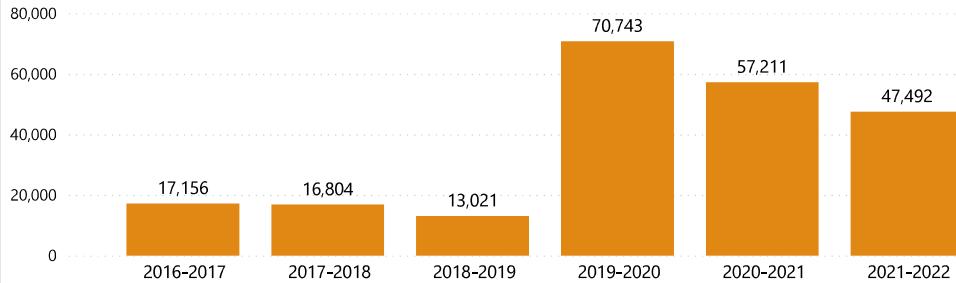


Top 5 States with houses completed but Amount not released fully

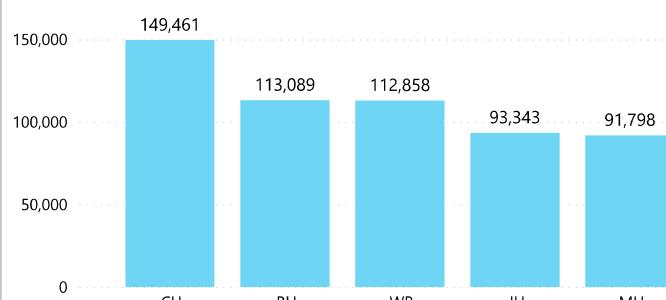

Bottom 5 States with houses completed but Amount not released fully

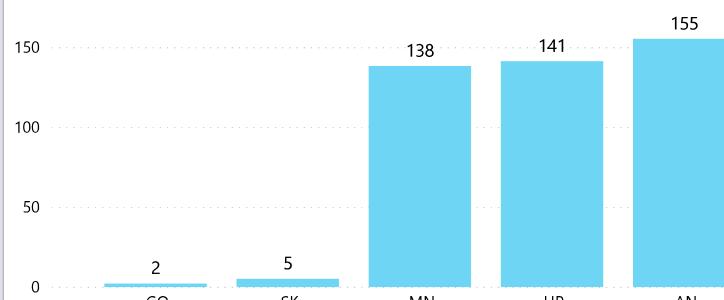







Top 5 Districts with houses completed but Amount not released fully

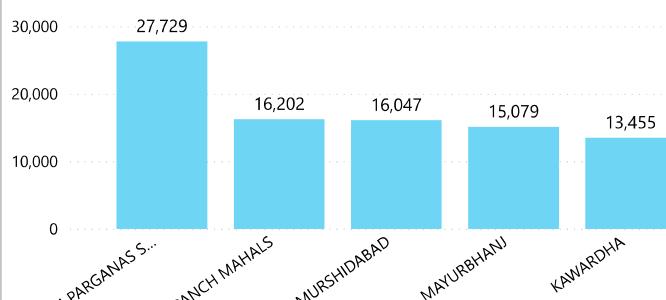

Bottom 5 Districts with houses completed but Amount not released fully



| MoRD Target (in No.) | Registered (in No.) | Geo-Tagged (in No.) | Sanctioned (in No.) | Completed (in No.) | Data Last refreshed on: 01-Jul-2022 |
|----------------------|---------------------|---------------------|---------------------|--------------------|-------------------------------------|
| 2,70,21,751 | 2,67,38,031 | 2,62,38,093 | 2,43,25,226 | 1,86,46,130 | Landless Report |

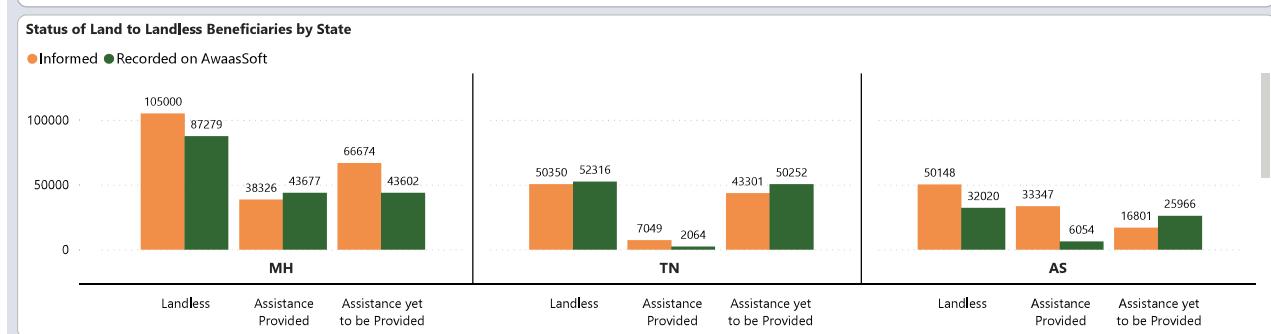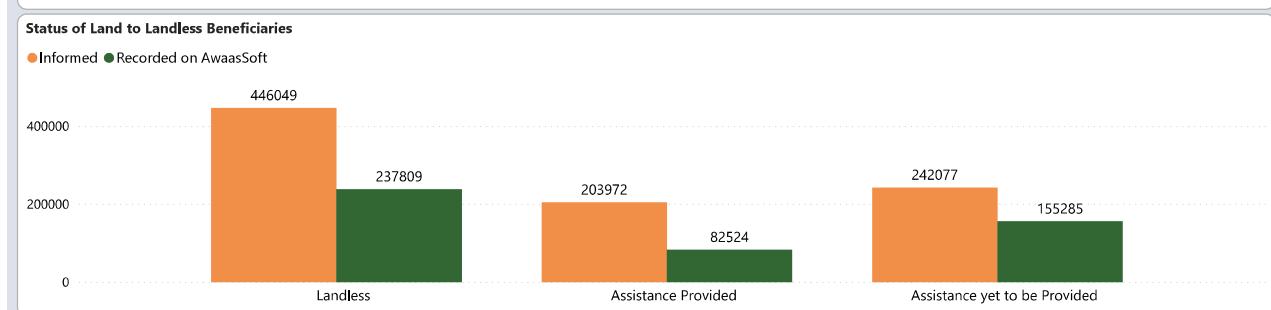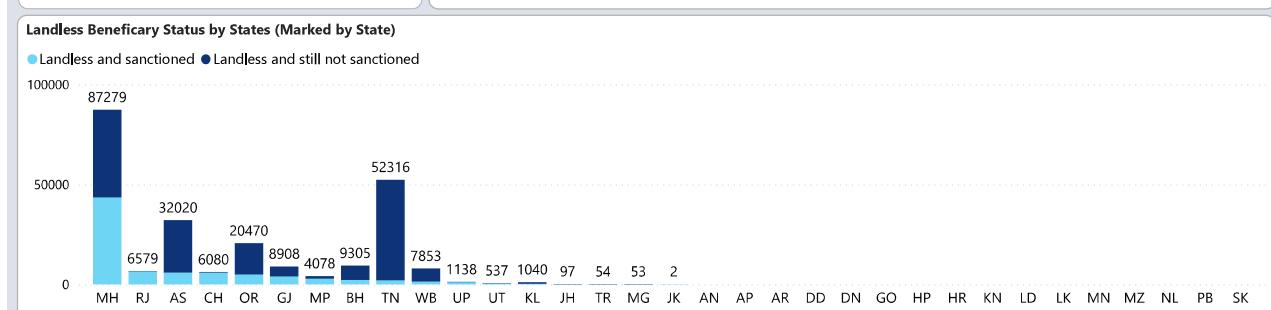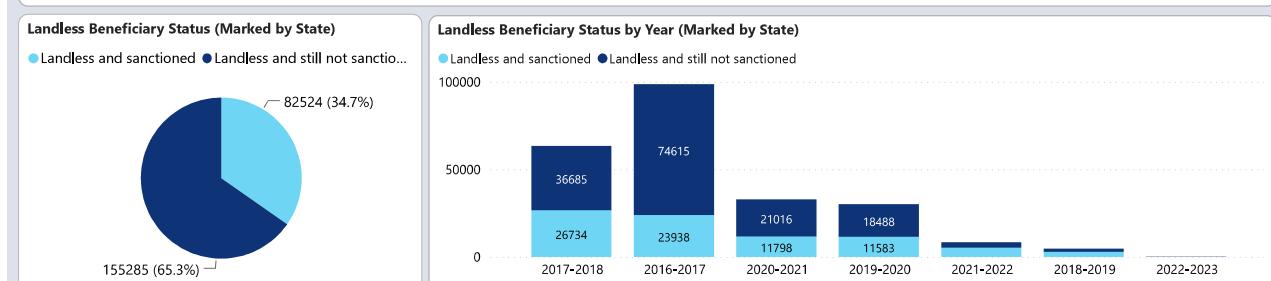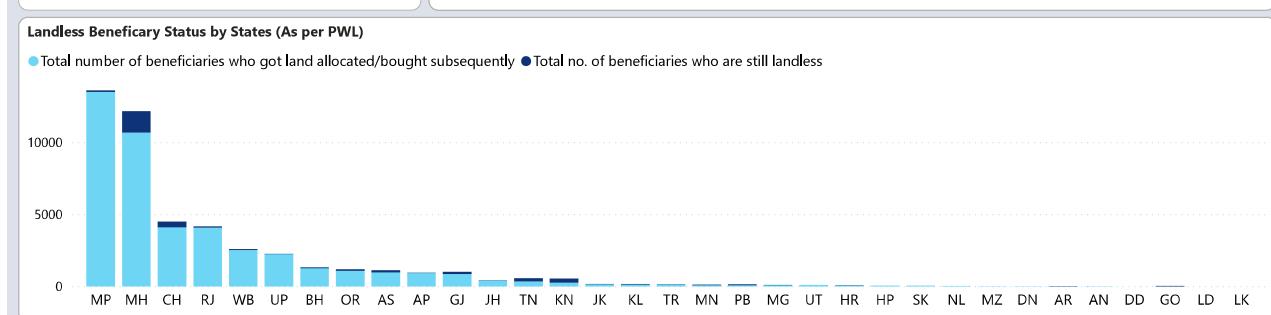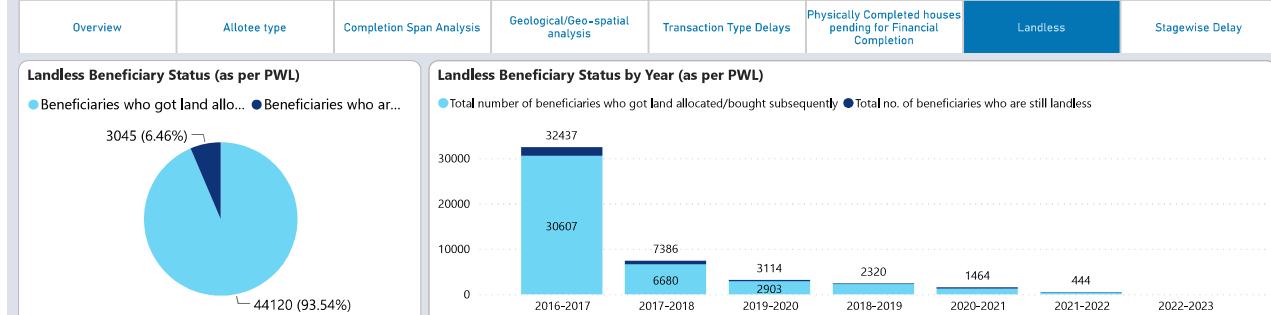

| MoRD Target (in No.) | Registered (in No.) | Geo-Tagged (in No.) | Sanctioned (in No.) | Completed (in No.) | Data Last refreshed on: 01-Jul-2022 | |
|----------------------|---------------------|---------------------|---------------------|--------------------|-------------------------------------|--|
| 2,70,21,751 | 2,67,38,031 | 2,62,38,093 | 2,43,25,226 | 1,86,46,130 | Report | |

Overview

Allottee type

Completion Span Analysis

Geological/Geo-spatial analysis

Transaction Type Delays

Physically Completed houses pending for Financial Completion

Landless


Stagewise Delay

Select Status: Multiple selections



Slabwise delay by state

0 to 15 Days ● 16 to 30 Days ● 1 to 2 Months ● 2 to 3 Months ● 3 to 6 Months ● 6 Months to 1 Year ● 1 Year and More

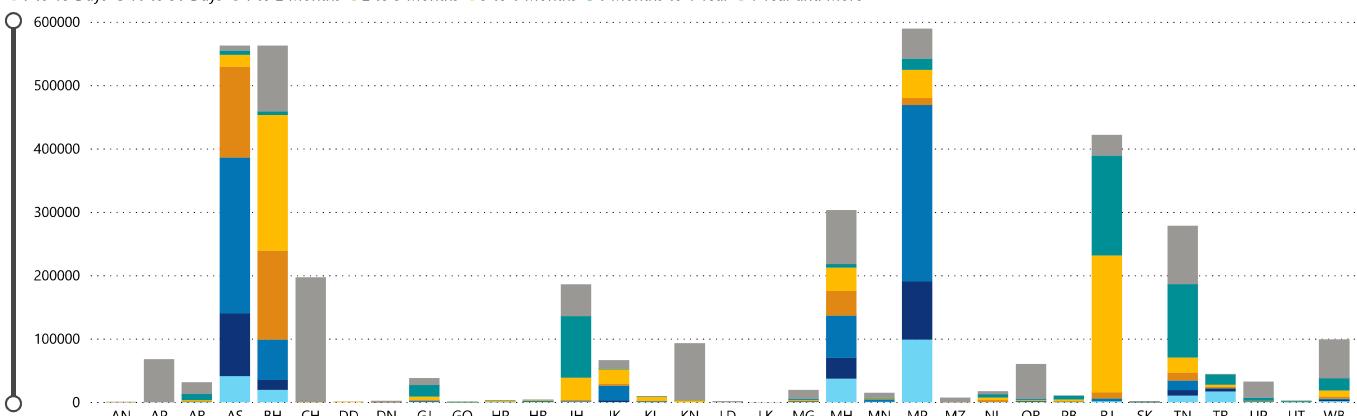

Select Slab: 6 Months to 1 Year



Stagewise delay by state

0 to 1500000

- Sanctioned to 1st installment released
- 1st installment released to 1st inspection mobile photo...
- 1st inspection mobile photo taken to 1st inspection ...
- 1st inspection mobile photo approval to 2nd installm...
- 2nd installment released to 2nd inspection mobile ph...
- 2nd inspection mobile photo taken to 2nd inspectio...
- 2nd inspection mobile photo approval to 3rd install...
- 3rd installment released to 3rd inspection mobile ph...
- 3rd inspection mobile photo taken to 3rd inspectio...
- 3rd inspection mobile photo approval to 4th install...
- 4th installment released to 4th inspection mobile ph...
- 4th inspection mobile photo taken to 4th inspectio...
- 4th inspection mobile photo approval to House com...

Select State: All



Slabwise delay by stages

0 to 15 Days ● 16 to 30 Days ● 1 to 2 Months ● 2 to 3 Months ● 3 to 6 Months ● 6 Months to 1 Year ● 1 Year and More

